

St Kevin's Community Hub

Newsletter



Issue – June 2025

Exciting progress at St Kevin's Community Hub

Progress of Works

Works continue to progress on programme with Kier having completed steel frame and sheathing board to the external envelope. We are currently making good progress towards getting the building wind and watertight with the roof substantially complete and brickwork underway.


Over the summer we will be installing the new MUGA Pitch, progressing the landscape works and commencing the internal fit out.

We will also be installing a new pedestrian crossing point on Coatbridge Road which will require temporary road closures whilst the works are taking place. Once a date for these works has been agreed with North Lanarkshire Council, Kier will issue a further newsletter to confirm arrangements.

We apologise for any inconvenience caused during these works and will endeavour to keep any disturbance to a minimum.

Jim Marsh (Project Manager, Kier Construction)

james.s.marsh@kier.co.uk

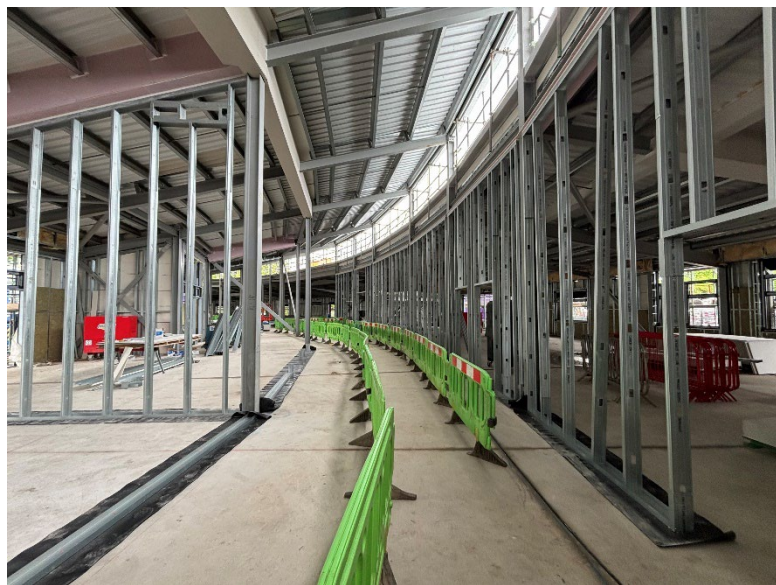

To view further details about the new development and the overall Town and Community Hub programme please visit the link below

<https://tinyurl.com/5x6chkhb>
